Act ID	Description	Stations	Original Duration	Rem Dur	Early Start	Early Finish	Total Float	%
1000	Mobilization		0	0	08SEP09 A			100
1010	East Creekside - Storm Sewer Installation	36+00 to 38+87	4d	0	08SEP09 A	11SEP09 A		100
1020	East Creekside - Pavement Installation (South)	32+00 to 38+87	10d	0	14SEP09 A	25SEP09 A		100
1021	Creekside Outfall Installation (Borco)		18d	0	28SEP09 A	21OCT09 A		100
1030	East Creekside - Pavement Installation (North)	32+00 to 38+87	20d	0	28SEP09 A	23OCT09 A		100
1032	East Creekside - Storm Sewer Installation	25+49 to 29+13	15d	0	05OCT09 A	23OCT09 A		100
1040	East Creekside - Sanitary Sewer Rehab (T Const)	27+63 to 31+00	5d	5d	02NOV09	06NOV09	136d	0
1050	West Creekside - Sanitary Sewer Rehab (T Const)	11+00 to 13+00	5d	5d	09NOV09	13NOV09	136d	0
1060	East Creekside - Pavement Installation (North)	25+49 to 31+24	15d	14d	26OCT09 A	13NOV09	105d	7
1062	East Creekside - Sanitary Sewer Rehab (T Const)	16+50 to 25+00	18d	18d	16NOV09	11DEC09	136d	0
1070	East Creekside - Pavement Installation (South)	25+49 to 31+24	13d	13d	16NOV09	04DEC09	141d	0
1071	West Creekside - Pavement Installation (West)	11+20 to 15+50	26d	26d	16NOV09	23DEC09	105d	0
1072	West Creekside - Pavement Installation (East)	11+20 to 15+50	23d	23d	28DEC09	29JAN10	105d	0
1075	East Creekside - Storm Sewer Installation	25+21 to 16+64	24d	24d	04JAN10 *	05FEB10	3d	0
1076	Eastside Circle - Storm Sewer Installation	39+86 to 42+70	9d	9d	08FEB10 *	19FEB10	90d	0
1077	East Creekside - Pavement Installation (West)	15+50 to 25+21	34d	34d	08FEB10 *	26MAR10	2d	0
1079	East Creekside - Pavement Installation (East)	15+50 to 25+21	29d	29d	29MAR10 *	07MAY10	1d	0
1120	Eastside Circle - Pavement Installation		34d	34d	10MAY10 *	25JUN10	0	0
1130	Demobilization		0	0		25JUN10	0	0

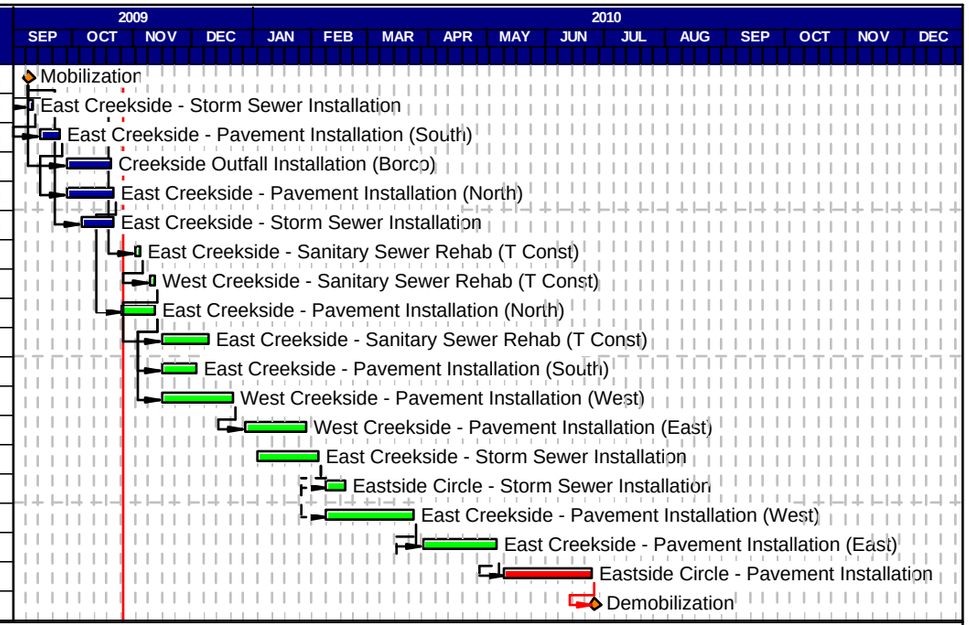

Start date	08SEP09
Finish date	25JUN10
Data date	27OCT09
Run date	27OCT09
Page number	1A

© Primavera Systems, Inc.

Metro City Construction, LP
Creekside Paving & Drainage Improv.

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point
